



# Newton North High School


## Project Areas by function / Current Construction Activity – 5/01/09

### Pool/Small gym (B) –

Concrete foundations and steel erection is complete - complete  
 Temporary weather protection and temporary heating – removal completed -  
 Concrete floor - level 1 and 2 complete  
 Plumbing roof drainage piping – ongoing – 80% complete  
 Underground plumbing – ongoing – 10% complete  
 Pool HVAC Dehumidification Equipment – delivery 5/1/09  
 Fireproof paint at structural steel – ongoing- 40% complete  
 Exterior Masonry – starting 5/11/09 +/-

### Academic (C)

Concrete floors: All levels - complete.  
 Interior spray on fireproofing – level 2 & 3 – completed. Underside of roof fireproofing – 100% complete. Ground level – 80% complete – completion will occur subsequent to low roof  
 Rough Mechanical/plumbing/ ductwork/electrical installation- Level 4 – 60% complete, Level 3 – 75% complete, Level 2 – 60% complete, Level 1 – 25 % complete.  
 Interior Masonry - level's 2 and 3 – 98% complete. Ground level 95% complete  
 Exterior Masonry – ongoing - 40% complete  
 Exterior framing, sheathing – 99% complete – exterior waterproofing ongoing – 75% complete  
 Permanent Roof Insulation work (except at low roof) – 100% complete.  
 Stair #5 installation completed – concrete treads placed 4/30/09

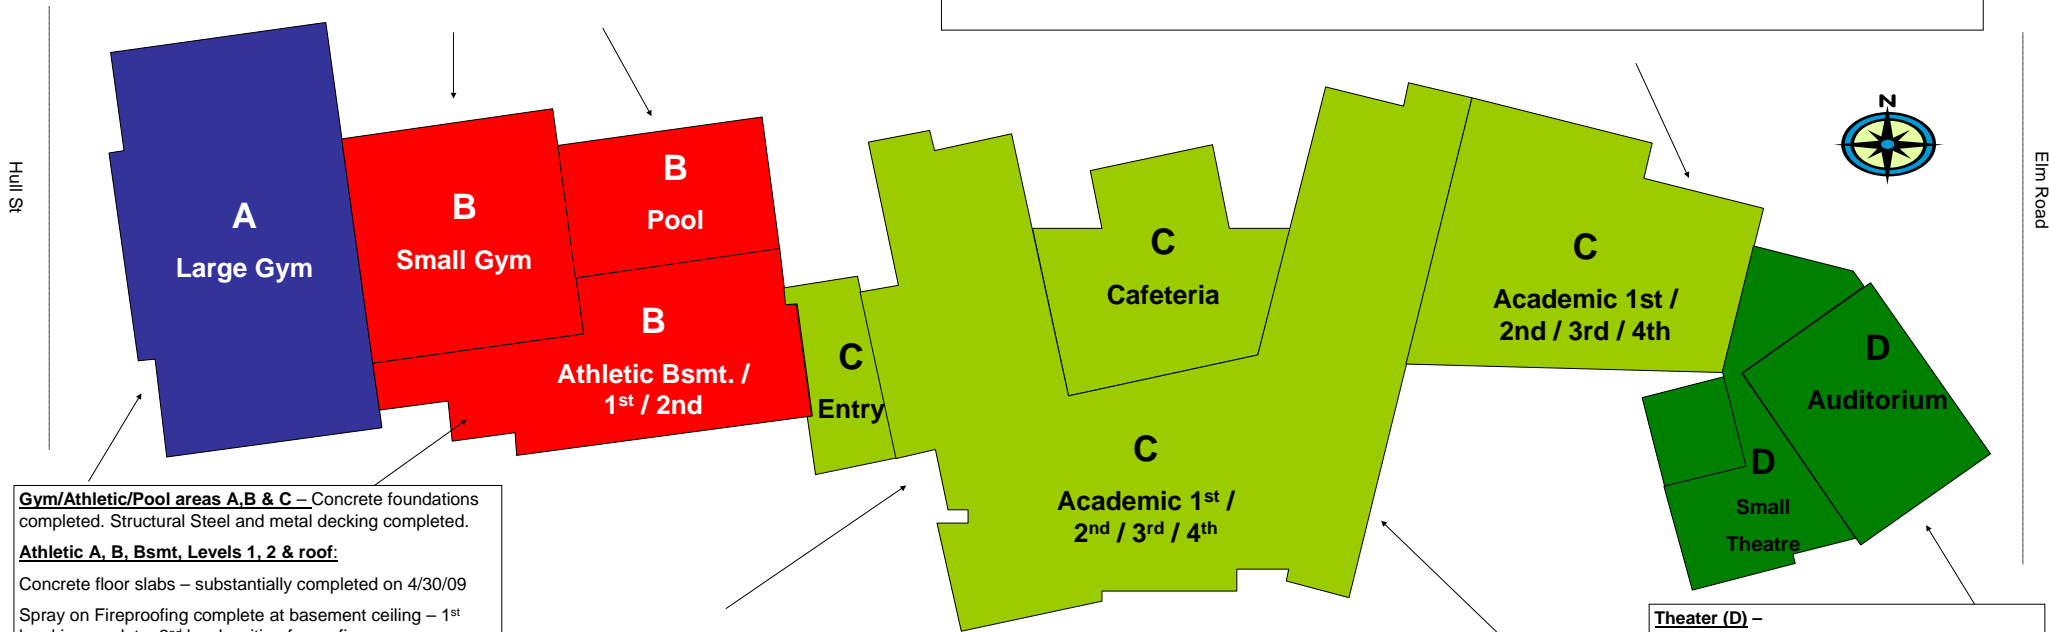

**Gym/Athletic/Pool areas A,B & C** – Concrete foundations completed. Structural Steel and metal decking completed.

### Athletic A, B, Bsmt, Levels 1, 2 & roof:

Concrete floor slabs – substantially completed on 4/30/09  
 Spray on Fireproofing complete at basement ceiling – 1<sup>st</sup> level is complete, 2<sup>nd</sup> level waiting for roofing  
 Plumbing rough in piping complete at basement locker rooms – 100% complete  
 Interior masonry – level 1- ongoing- 60 % complete, basement – ongoing – 35%  
 Roof parapet framing ongoing– 90%  
 Wall framing and sheathing ongoing – 55%  
 Stair #1 – started – 40% complete  
 Permanent roof insulation installation – Athletic “B” roof – 5/5/09, Athletic A – 5/18/09 (permanent insulation/roofing)  
 Removal of temporary winter protection – complete  
 Elevator A – start installation week of 5/11/09

### Academic (C) / Cafeteria (C):

Rough Mechanical/plumbing/ ductwork/electrical installation: ongoing: level 4- 99% complete. Level 3 -98% complete, Level 2 – 96% complete, Level 1 -88% complete.  
 Exterior framing, sheathing – ongoing – 98% complete / Exterior flashings and waterproof barrier ongoing – 88% complete.  
 Interior metal stud framing – 90% complete. 3<sup>rd</sup> floor ready for drywall installation - start contingent on window installation  
 Window delivery – ongoing – installation to commence on 5/4/09.  
 Interior masonry partitions – ongoing – 98% complete  
 Exterior Masonry – Brick work started week of 2/2/09 – ongoing – 85% complete  
 Winter weather protection and temporary heating removal - complete  
 Permanent roof insulation / Temporary roof – 100% of main complete.  
 Delivery and installation of roof top HVAC Units – Area C is complete.  
 Elevator B – started 4/23/09

### Theater (D) –

Perimeter concrete foundations and structural steel - complete  
 Miscellaneous concrete Control room, stage and orchestra pit walls complete 100%. Second floor – concrete & stage roof – placed 4/27/09  
 Concrete stage – installation week of 5/11/09+/-  
 Underground piping work - complete.  
 Concrete floor at small theater - complete  
 Fireproofing paint @ structural steel– ongoing– 75% complete  
 HVAC equipment (chiller) set in place - week of 4/6, piping ongoing  
 Masonry - Exterior – started 4/13 – ongoing – 25% complete. Masonry – Interior- ongoing – 20% complete
